MINI TEST PLAN AND ESTIMATE

Fictional Mobile Wellness App: **MindfulMe**

Prepared by	Maryam Masood
Registration number	OCT26-SQ06-01
Date	27 October 2026
Planned testing window	2 weeks / 10 working days
Reference	User-provided MindfulMe UI concept image

Project purpose: define a practical, risk-based QA plan and estimate the effort needed to test the supplied fictional app design.

1. Project Overview

Application summary. MindfulMe is a fictional mobile wellness app with onboarding, a home dashboard, meditation sessions, a mood journal, personal goals, mood tracking, profile settings and a success screen.

Testing objectives

• Verify core user journeys and expected behavior of the MindfulMe mobile app.

• Identify functional, usability, compatibility, accessibility and data-handling defects.

• Confirm goals, mood entries and journal entries are saved and displayed accurately.

• Provide a test summary and release recommendation based on exit criteria.

2. Scope

In scope

• Welcome, sign-up/login and navigation

• Home dashboard and quick actions

• Meditation session listing and playback controls

• Journal mood selection, text entry, photo attachment UI and save behavior

• Goals creation, progress updates and completion state

• Mood calendar, mood insights and chart display

• Profile, edit profile, settings, notifications and privacy screens

• Success/confirmation screen and return-to-home navigation

• Basic usability, responsive layout, accessibility and network/error handling

Out of scope

• Clinical validation of meditation or mental-health content

• Penetration testing and formal security certification

• Production-scale load testing

• Third-party payment processing (not shown in supplied design)

3. Test Modules and Approach

Module	Approach
Onboarding & Authentication	Positive/negative tests, required fields, invalid credentials, navigation and session checks
Home Dashboard	Verify greeting, daily goals, progress values, quick actions and bottom navigation
Meditation	Check categories, session titles/durations, play/pause, back navigation and unavailable audio handling
Journal & Mood	Validate mood choices, 500-character limit, empty entry, save behavior and optional photo UI
Goals	Create/view goals, progress updates, due dates, invalid/blank input and personal/wellness filters
Mood Tracker & Insights	Date navigation, mood selection, chart totals, empty state and month boundary behavior
Profile & Settings	Profile editing, notification/settings navigation, privacy/help links and logout
UI, Compatibility & Accessibility	Screen sizes, orientation, text scaling, contrast, touch targets, offline/error states

4. Entry and Exit Criteria

Entry criteria

• Approved requirements/design reference and testable build are available.

• Test device(s), test accounts and required test data are ready.

• Critical user flows and expected results have been agreed with the team.

• Build installs and opens without a blocker.

Exit criteria

• 100% of planned critical test cases executed.

• At least 95% of all planned test cases executed.

• No open Critical or High severity defects; any exception formally accepted.

• All failed tests have linked defect records and evidence.

• Test summary, known risks and release recommendation are shared.

5. Two-Week Schedule

Day / Date	Planned activity	Hours
Day 1 2026-10-27	Review design, define scope, risks and assumptions	5
Day 2 2026-10-28	Prepare test plan, scenarios and test data	6
Day 3 2026-10-29	Write onboarding, home and navigation test cases	6
Day 4 2026-10-30	Write meditation, journal and mood test cases	6
Day 5 2026-11-02	Write goals, profile, compatibility test cases; review	6
Day 6 2026-11-03	Build smoke test, environment check and test execution	6
Day 7 2026-11-04	Execute core functional tests; log defects	6
Day 8 2026-11-05	Execute negative, boundary, usability and compatibility tests	6
Day 9 2026-11-06	Retest fixes, run regression tests, verify exit criteria	5
Day 10 2026-11-09	Complete report, summarize risks and share deliverables	4

Note: schedule dates exclude the weekend of 31 Oct–1 Nov 2026.

6. Three-Point Estimation (PERT)

For each task, estimate optimistic (O), most likely (M), and pessimistic (P) effort. The expected estimate is: **(O + 4M + P) / 6**. Estimates are person-hours and are planning assumptions, not measured actuals.

Task	O	M	P	Expected hrs
Scope and requirements review	2	3	5	3.17
Test planning and risk analysis	3	5	8	5.17
Test case design	6	9	14	9.33
Test data and environment setup	2	4	7	4.17
Functional test execution	8	12	18	12.33
Usability and compatibility testing	3	5	9	5.33
Defect reporting and retesting	3	6	10	6.17
Regression testing	3	5	8	5.17
Test summary and report	2	3	5	3.17
TOTAL				**54.00**

Estimated total: 54.00 person-hours. Add contingency if requirements, platform coverage or test environment change materially.

7. Risks and Mitigations

• **Only design screenshots are available; behavior may differ in the actual build.** Mitigation: Confirm requirements and verify behavior on the running build.


• **Backend or media services may be unavailable.** Mitigation: Use stable test environment and record blocked tests clearly.

• **Late build changes reduce regression time.** Mitigation: Prioritize critical journeys and reserve Day 9 for retesting/regression.

• **Personal journal data is sensitive.** Mitigation: Use synthetic test data and verify logout/privacy behavior.

8. Practical Steps and UI Evidence

Single screenshot showing all eight MindfulMe UI screens from the supplied design collage. This is design-reference evidence, not proof of live app execution.

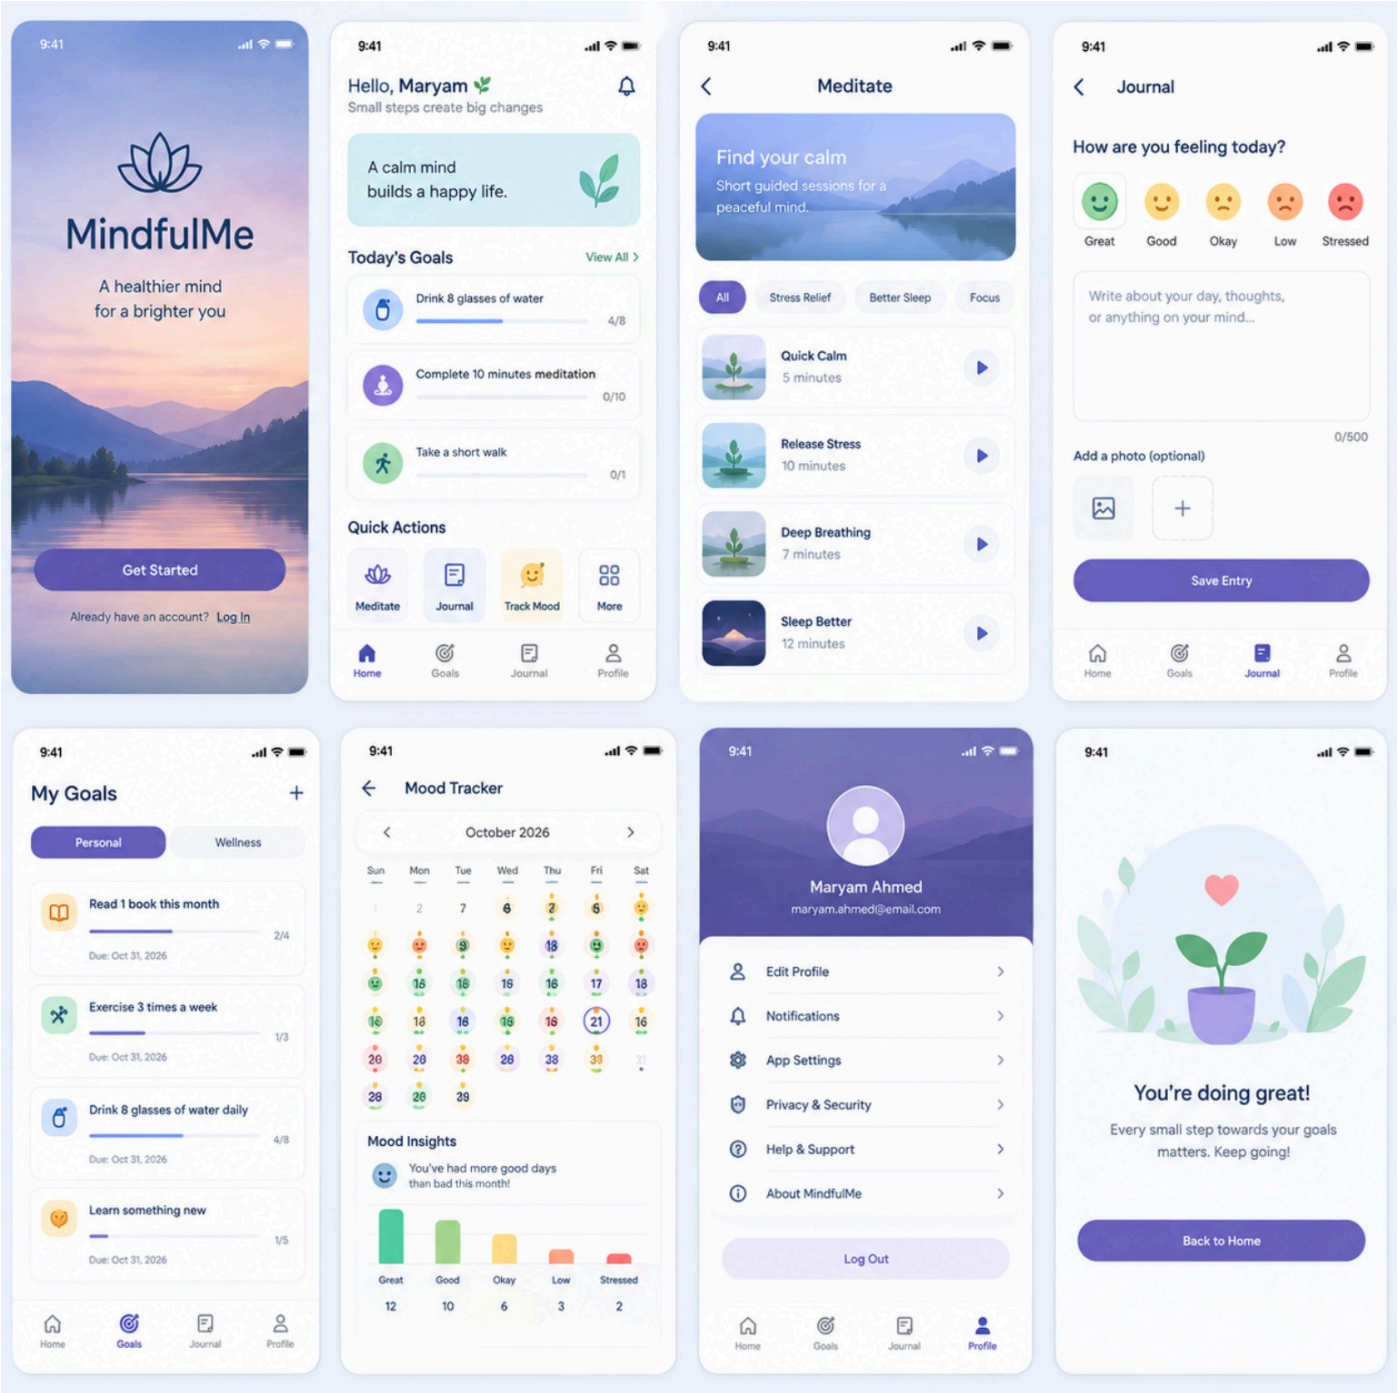

9. Deliverables and Reporting

Project files included in this package:

• MindfulMe_Mini_Test_Plan_Report.pdf — this report and design-reference evidence.

• MindfulMe_Test_Estimation.xlsx — three-point estimation, two-week schedule, modules and criteria.

• MindfulMe_Test_Plan.json — structured project plan, scope, schedule, criteria, risks and estimate inputs.

Reporting note: No functional test execution results are claimed because the supplied artifact is a UI concept image rather than a running app. When a build is available, add test case IDs, actual results, pass/fail/blocked status, defect IDs, severity, and execution screenshots.

Prepared by: Maryam Masood | Registration: OCT26-SQ06-01 | Date: 27 October 2026
